




UNDER CONSTRUCTION

Newaygo Series 2 Construction Progress




Project Duration is 35% Complete



Updated Cafetorium in Phase I



Updated Science Room in Phase 2

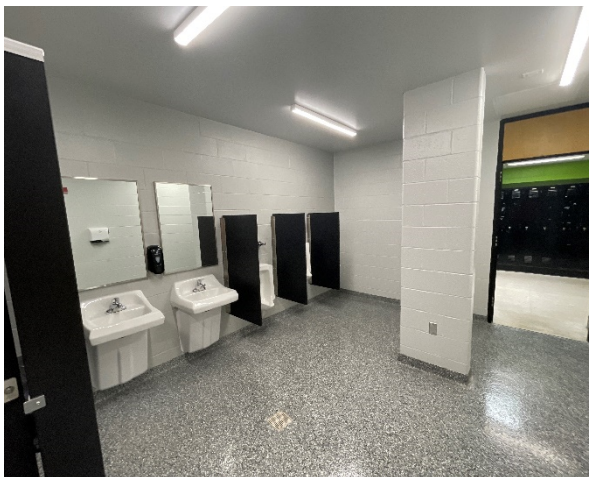

Updated Group Bathrooms

WORK IN PROGRESS

This Month (September)

- Cafetorium
 - Stage curtain install
 - AC Start Up
 - Complete lighting controls
- Fall Renovations (A Wing)
 - Complete underground plumbing and backfill
 - Install above ceiling ductwork
 - Install new mechanical units
 - Run new MEP above ceiling
 - Concrete floor infills

Next Month (October)

- Fall Renovations (A Wing)
 - Begin resinous flooring
 - Ceiling grid
 - Paint classrooms
 - Install new mechanical units
- Mechanical Room
 - Installation of new boiler (Fall 2026)

PROJECT MANAGEMENT UPDATE

Safety

- This month's Safety Goal focuses on safe excavation practices. Being aware of all known and potential underground utilities. Taking the time to plan, communicate, and verify.

Schedule

- The project is on schedule


Other Progress

- Boiler replacement at the MS in progress
- Gathering geotechnical analysis for new MS Parking Lot
- Summer renovation punch list



UNDER CONSTRUCTION

Newaygo Series 2 Construction Progress



Football Field Sidewalk Relocation



Phase I A-Wing Overview



Updated Classroom in Phase 2



Updated Main HS Entrance



New Carpet in B-Wing Hallway





Phase 3 Ductwork Install



UNDER CONSTRUCTION

Newaygo Series 2 Construction Progress

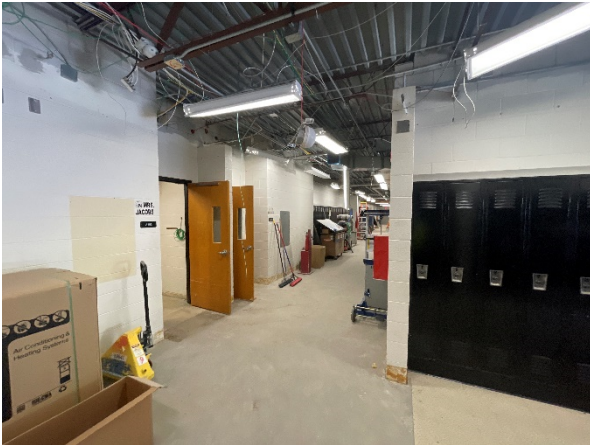

Phase 3 Hallway Overview



Phase 3 Classroom Mechanical Preparation



Cafetorium Stage Curtain Install



Phase 3 Bathroom UG Plumbing
