Newaygo Series 2 Construction Progress

PROJECT UPDATE UNDER CONSTRUCTION

Project Duration is 50% Complete



Phase 3 Classroom Overview



Phase 3 Classroom Overview



Phase 3 New Single Bathroom

WORK IN PROGRESS

This Month (November)

- Cafetorium
  - Coordinating lighting controls training
- Fall Renovations (A Wing)
  - Polished concrete
  - Install ceiling tiles
  - Paint classrooms
  - Bathroom fixtures
  - Final electrical and mechanical connections

Next Month (December)

- Fall Renovations (A Wing)
  - Begin hallway carpet
  - Final cleaning
  - Phase 3 punch list
  - School furniture relocating
- Mechanical Room
  - Installation of new boiler

PROJECT MANAGEMENT UPDATE

Safety

- This month's Safety Goal focuses on winter jobsite preparation. Being aware of all known and potential hazards and taking the time to prepare. Keeping our people and jobsites safe this winter.

Schedule

- The project is on schedule

Other Progress

- Gathering geotechnical analysis for new MS parking lot complete.
- Summer renovation punch list (90% complete)

Newaygo Series 2
Construction Progress



Wood Shop Overview



Phase 3 Photography Studio Overview



STEM and Wood Shop Polished Concrete



Updated Main HS Entrance



Phase 3 Wood Shop Classroom Overview



Phase 3 Classroom Overview

PROJECT UPDATE UNDER CONSTRUCTION

Newaygo Series 2
Construction Progress



Phase 3 Classroom Overview



Wood Shop Room Polished Concrete



New Wood Door Install

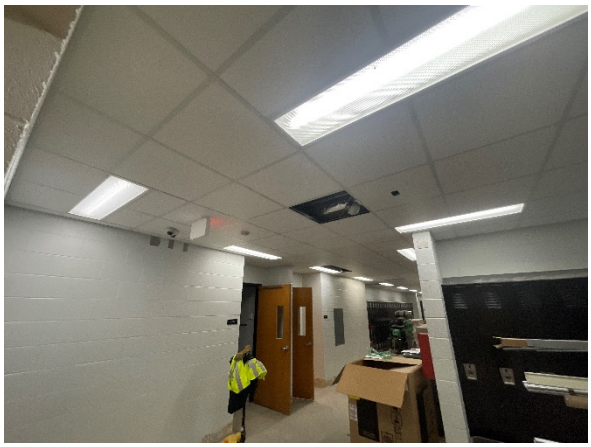

Phase 3 Hallway Ceiling Overview
