
Newaygo Series 2
Construction Progress

PROJECT UPDATE UNDER CONSTRUCTION

Project Duration is 40% Complete



Overview of Janitors Closet in Phase 3

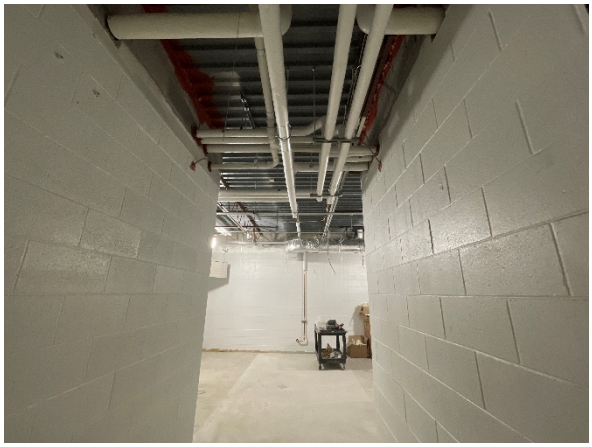

New Windows in Phase 3



Acoustical Spray Ceiling in Wood Shop

WORK IN PROGRESS

This Month (October)

- Cafetorium
  - Lighting controls training
- Fall Renovations (A Wing)
  - Polished concrete
  - Install above ceiling ductwork
  - Install new mechanical units
  - Run new MEP above ceiling
  - Resinous flooring

Next Month (November)

- Fall Renovations (A Wing)
  - Begin classroom carpet
  - Install ceiling tiles
  - Paint classrooms
  - Bathroom fixtures
- Mechanical Room
  - Installation of new boiler (Fall 2026)

PROJECT MANAGEMENT UPDATE

Safety

- This month's Safety Goal focuses on hidden hazards. Being aware of all known and potential trip hazards. Taking the time to identify and eliminate these hazards.

Schedule

- The project is on schedule

Other Progress

- Boiler replacement at the MS is complete.
- Gathering geotechnical analysis for new MS Parking Lot
- Summer renovation punch list

PROJECT UPDATE UNDER CONSTRUCTION

Newaygo Series 2
Construction Progress



New Metal Panel Facia



Concrete Pad Outside of Wood Shop



Classroom Ceiling Grid Install in Phase 3



Updated Main HS Entrance




New Doorway Between Classrooms



Phase 3 Sideway Replacement

PROJECT UPDATE UNDER CONSTRUCTION

Newaygo Series 2
Construction Progress

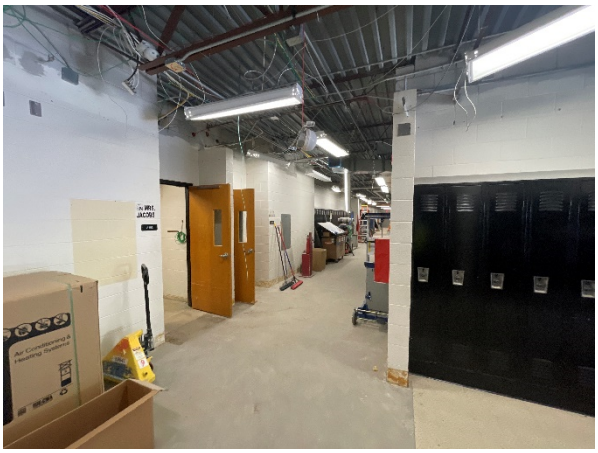

Phase 3 Hallway Overview



Phase 3 Classroom Mechanical Preparation



Classroom Overview in Phase 3



Phase 3 Polished Concrete Preparation
